


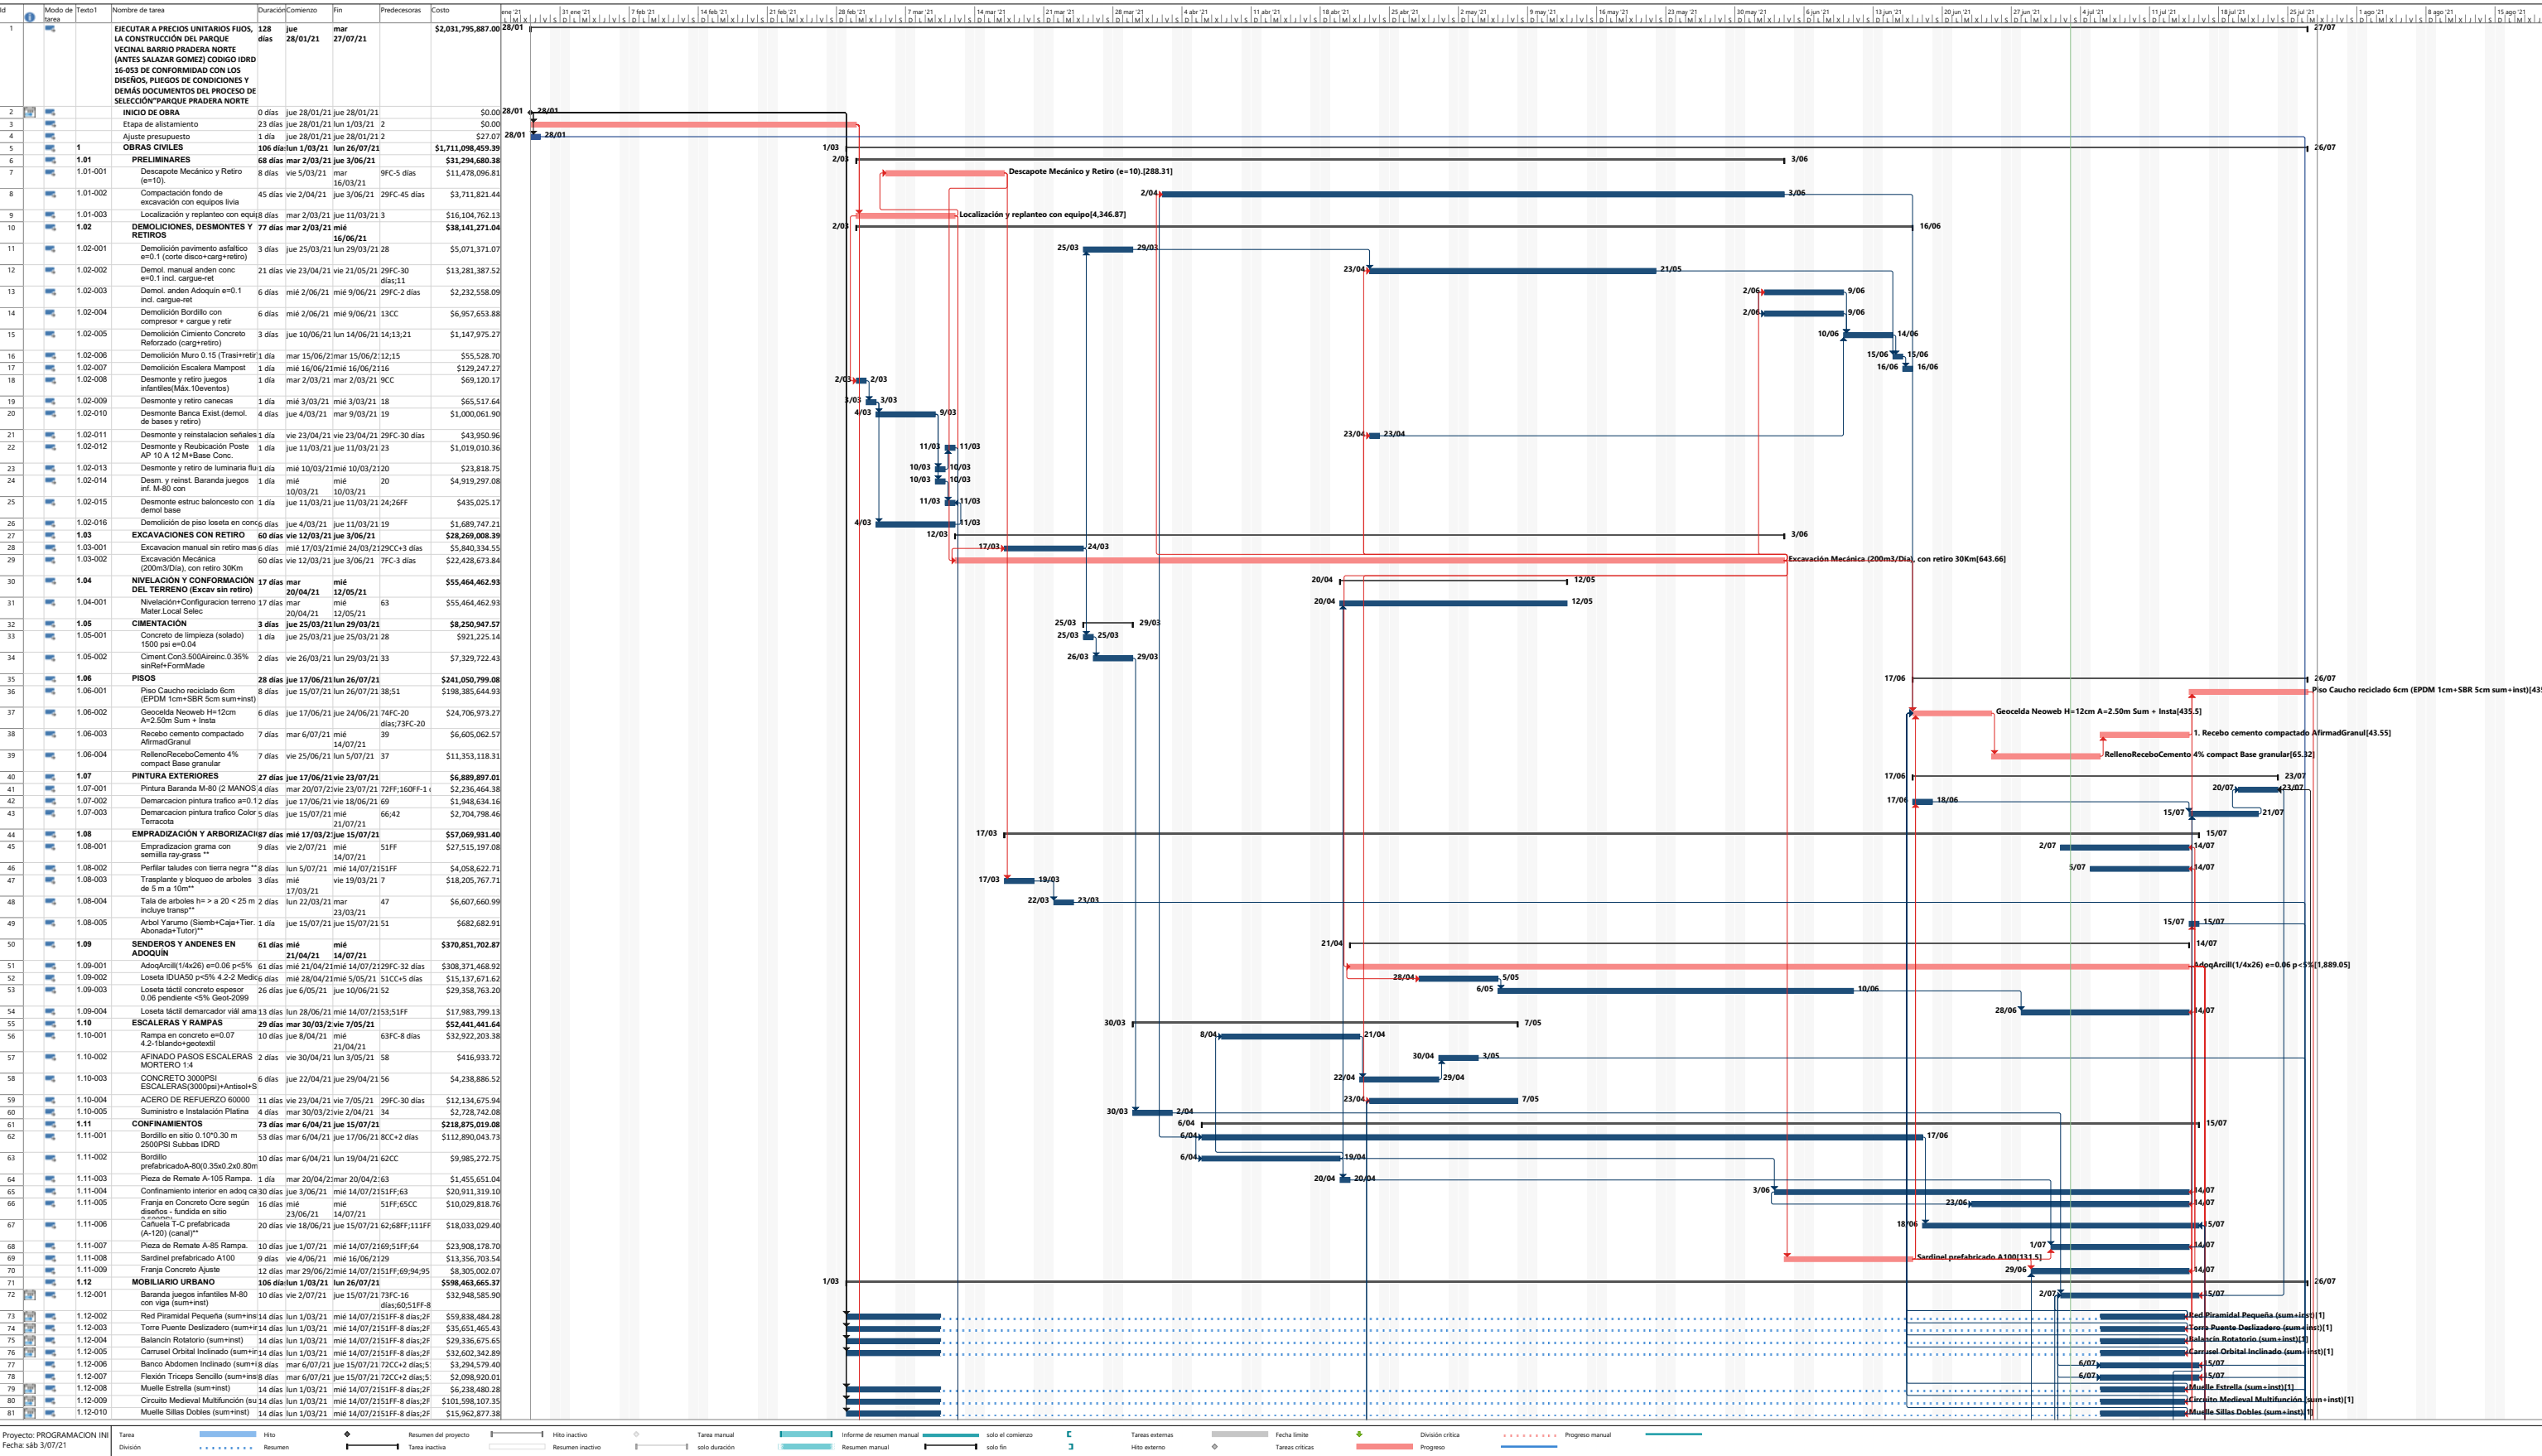

| Id  | Modo de tarea | Texto1   | Nombre de tarea                                       | Duración | Comienzo     | Fin          | Predecesoras         | Costo            |  | 1 feb 21 | 31 mar 21 | 7 feb 21 | 14 feb 21 | 21 feb 21 | 28 feb 21 | 7 mar 21 | 14 mar 21 | 21 mar 21 | 28 mar 21 | 4 abr 21 | 11 abr 21 | 18 abr 21 | 25 abr 21 | 2 may 21 | 9 may 21 | 16 may 21 | 23 may 21 | 30 may 21 | 6 jun 21 | 13 jun 21 | 20 jun 21 | 27 jun 21 | 4 jul 21 | 11 jul 21 | 18 jul 21 | 25 jul 21 | 1 ago 21 | 8 ago 21 | 15 ago 21 |  |
|-----|---------------|----------|-------------------------------------------------------|----------|--------------|--------------|----------------------|------------------|--|----------|-----------|----------|-----------|-----------|-----------|----------|-----------|-----------|-----------|----------|-----------|-----------|-----------|----------|----------|-----------|-----------|-----------|----------|-----------|-----------|-----------|----------|-----------|-----------|-----------|----------|----------|-----------|--|
| 82  |               | 1.12-013 | Modulo Domina (sum+inst)                              | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$9,983,911.08   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 83  |               | 1.12-014 | Multifuncional 6 Torres (sum+inst)                    | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$74,657,938.41  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 84  |               | 1.12-015 | Modulo Barra Fija Abdomen (sum                        | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$3,896,329.24   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 85  |               | 1.12-016 | Modulo Remo (sum+inst)                                | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$7,107,932.84   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 86  |               | 1.12-017 | Modulo Sky (sum+inst)                                 | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$6,477,152.03   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 87  |               | 1.12-018 | Prensa de Pecho - Jalón Espalda (sum+inst)            | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;51FF-8   | \$8,522,209.83   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 88  |               | 1.12-019 | Modulo Escalador (sum+inst)                           | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$8,141,659.76   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 89  |               | 1.12-020 | 1-Doble (sum+inst)                                    | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$26,867,627.35  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 90  |               | 1.12-021 | Doble Flexión Pierna (sum+inst)                       | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$26,867,627.35  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 91  |               | 1.12-023 | ESTACIÓN DE AJEDREZ URBANO (sum+inst)                 | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;51FF-8   | \$18,178,976.32  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 92  |               | 1.12-024 | Banca en concreto Rectangular 2.00X.50m (sum+inst)    | 8 dias   | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;51FF-8   | \$13,696,132.88  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 93  |               | 1.12-025 | Banca en concreto 0.60X0.80m                          | 18 dias  | mar 6/07/21  | jue 15/07/21 | 72CC+2 dias;5        | \$6,036,000.56   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 94  |               | 1.12-026 | Muro BANCA 60cm                                       | 19 dias  | mié 28/04/21 | lun 24/05/21 | 59CC+3 dias          | \$15,407,684.24  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 95  |               | 1.12-027 | Muro BANCA 40cm                                       | 34 dias  | mié 28/04/21 | lun 14/06/21 | 59CC+3 dias          | \$46,137,842.12  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 96  |               | 1.12-028 | Caneaca doble acero inoxidable                        | 1 dias   | vie 2/07/21  | mar 6/07/21  | 72CC                 | \$6,554,346.08   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 97  |               | 1.12-029 | Golosa                                                | 1 dia    | lun 26/07/21 | lun 26/07/21 | 36FF                 | \$359,736.71     |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 98  |               | 1.13     | SEÑALIZACIÓN                                          | 3 dias   | mié 14/07/21 | vie 16/07/21 |                      | \$4,035,632.64   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 99  |               | 1.13-001 | SEÑAL ORIENTADO 30X1.70 (SUM + INST)                  | 1 dia    | mié 14/07/21 | mié 14/07/21 | 77FC-2 dias          | \$1,424,116.74   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 100 |               | 1.13-002 | Señal Informativa 1 Cara (SUM + INST)                 | 1 dia    | jue 15/07/21 | jue 15/07/21 | 99                   | \$1,138,021.42   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 101 |               | 1.13-003 | Señal plano ubicación parque (SUM + INST)             | 1 dia    | vie 16/07/21 | vie 16/07/21 | 100                  | \$1,473,494.48   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 102 |               | 2        | REDES                                                 | 80 dias  | vie 12/03/21 | jue 1/07/21  |                      | \$311,845,516.27 |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 103 |               | 2.1      | REDES HIDRO SANITARIAS                                | 25 dias  | vie 12/03/21 | jue 15/04/21 |                      | \$127,665,243.85 |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 104 |               | 2.1-001  | Excavacion manual sin retro mas                       | 10 dias  | vie 12/03/21 | jue 25/03/21 | 9                    | \$5,271,318.25   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 105 |               | 2.1-002  | Tuberia PVC, ALL 4" Exca y relleno recebo **          | 3 dias   | mar 23/03/21 | jue 25/03/21 | 104FC-3 dias         | \$6,470,919.00   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 106 |               | 2.1-003  | Tuberia Novafort d=160mm **                           | 9 dias   | vie 26/03/21 | mié 7/04/21  | 105                  | \$14,021,410.65  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 107 |               | 2.1-004  | Tuberia d=10" 250 MM NOVAFOf4                         | 5 dias   | vie 26/03/21 | mié 31/03/21 | 104                  | \$7,171,217.70   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 108 |               | 2.1-005  | Caja de inspeccion 0.60mX0.80m                        | 2 dias   | vie 26/03/21 | jue 2/04/21  | 104                  | \$4,778,548.11   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 109 |               | 2.1-006  | Caja de inspeccion 0.80mX0.80m                        | 2 dias   | vie 26/03/21 | lun 29/03/21 | 104                  | \$1,338,645.38   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 110 |               | 2.1-007  | Filtro geodren planar tuberia 100 mm h=1.0 **         | 12 dias  | vie 19/03/21 | lun 5/04/21  | 104FC-5 dias         | \$42,156,912.00  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 111 |               | 2.1-008  | SumideroCaja LateralSL-100 en C6                      | 6 dias   | lun 5/04/21  | lun 12/04/21 | 108                  | \$21,289,591.39  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 112 |               | 2.1-009  | Corte en asfalto con cortadora disco 14"              | 1 dia    | mié 24/03/21 | mié 24/03/21 | 104FC-2 dias         | \$250,642.08     |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 113 |               | 2.1-010  | Demol pav asfaltico e=0.1                             | 1 dia    | jue 25/03/21 | jue 25/03/21 | 112                  | \$321,547.23     |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 114 |               | 2.1-011  | Reposicion en asfalto                                 | 1 dia    | jue 15/04/21 | jue 15/04/21 | 118;134              | \$1,477,430.37   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 115 |               | 2.1-012  | Pozo de Inspeccion A.L.L. - red de Desagües           | 6 dias   | mié 31/03/21 | mié 7/04/21  | 116                  | \$9,423,861.45   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 116 |               | 2.1-013  | Caja de Inspeccion A.L.L. - red de Desagües           | 1 dia    | mar 30/03/21 | mar 30/03/21 | 109                  | \$906,162.33     |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 117 |               | 2.1-014  | Tuberia P.V.C - A.L.L.10" - red de Desagües           | 3 dias   | jue 1/04/21  | lun 5/04/21  | 107                  | \$7,339,188.37   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 118 |               | 2.1-015  | Recibo cemento compactado AfirmaGbrand                | 5 dias   | jue 8/04/21  | mié 14/04/21 | 117;106;110;1        | \$5,447,849.54   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 119 |               | 2.2      | REDES ELECTRICAS                                      | 80 dias  | vie 12/03/21 | jue 1/07/21  |                      | \$184,180,272.41 |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 120 |               | 2.2-001  | Ducteria Enterrada PVC 2 Ø3"                          | 16 dias  | mié 17/03/21 | mié 19/05/21 | 131;105;131CC+3 dias | \$27,549,493.20  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 121 |               | 2.2-002  | Cámara de Inspección Cuadrada según CS 274 de CODENSA | 14 dias  | mié 24/03/21 | vie 21/05/21 | 131;120FC-15d dias   | \$20,870,158.75  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 122 |               | 2.2-003  | Poste M-130 (Sum+instal)**                            | 6 dias   | lun 24/05/21 | lun 31/05/21 | 121;114              | \$27,841,421.66  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 123 |               | 2.2-004  | Luminaria (24 Leds) 15W-700mA-2 dias                  | 2 dias   | mar 15/06/21 | mié 16/06/21 | 138                  | \$9,273,058.80   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 124 |               | 2.2-005  | Luminaria (24 Leds) 52W-700mA-4 dias                  | 4 dias   | jue 17/06/21 | mar 22/06/21 | 123                  | \$27,625,038.28  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 125 |               | 2.2-006  | Luminaria (24 Leds) 56W-700mA-2 dias                  | 2 dias   | mié 23/06/21 | jue 24/06/21 | 124                  | \$10,037,071.15  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 126 |               | 2.2-007  | Luminaria (24 Leds) 66W-700mA-1 dia                   | 1 dia    | vie 25/06/21 | vie 25/06/21 | 125;136FF            | \$2,291,992.42   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 127 |               | 2.2-008  | Cable 3N*4 AWG (Sum+instal) Al                        | 10 dias  | mar 1/06/21  | lun 14/06/21 | 122;129              | \$3,556,866.00   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 128 |               | 2.2-009  | BAJANTE EN TUBO IMC Ø2" (Inc-1                        | 1 dia    | lun 24/05/21 | lun 24/05/21 | 121                  | \$278,484.70     |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 129 |               | 2.2-010  | Barraje BT prefabricado 500 A 6x12, para caja CS      | 3 dias   | mar 25/05/21 | jue 27/05/21 | 128                  | \$2,547,224.00   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 130 |               | 2.2-011  | SIST PUESTA A TIERRA SIE                              | 1 dia    | lun 28/06/21 | lun 28/06/21 | 126                  | \$2,740,642.92   |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 131 |               | 2.2-012  | Excavacion manual sin retro mas                       | 8 dias   | vie 12/03/21 | mar 23/03/21 | 9;141FF              | \$563,795.96     |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
| 132 |               | 2.2-013  | Corte en asfalto con cortadora                        | 1 dia    | mié 24/03/21 | mié 24/03/21 | 1                    |                  |  |          |           |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |           |           |          |           |           |           |          |           |           |           |          |          |           |  |
