ENTREGA DE PRODUCTOS Y/O SERVICIOS OBTENIDOS DE LA EJECUCIÓN DEL CONTRATO DE OBRA No.

CO1.PCCNTR.8212249

OBJETO DEL CONTRATO	Realizar adecuaciones integrales a todo costo para la infraestructura de la sede "Ciudad Verde" del Centro Industrial y de Desarrollo Empresarial de Soacha, incluyendo suministro de materiales, mano de obra y servicios técnicos especializados.
CONTRATISTA DE OBRA	CONSORCIO AGH–C&C–SEIPRODEG CIUDAD VERDE
INTERVENTOR	JOHAN JAVIER OÑATE NUÑEZ
SUPERVISOR	EDWARD FABIAN MEDINA BARAJAS
LUGAR DE EJECUCION	SOACHA - CUNDINAMARCA
FECHA DE INICIO DEL CONTRATO	03/09/2025
FECHA PRESENTE ACTA	30/12/2025

El interventor JOHAN JAVIER OÑATE NUÑEZ en desarrollo de sus actividades y en coordinación con el proveedor CONSORCIO AGH–C&C–SEIPRODEG CIUDAD VERDE, hace constar la entrega de los siguientes ítems y/o productos para el proyecto denominado ·Realizar adecuaciones integrales a todo costo para la infraestructura de la sede "Ciudad Verde" del Centro Industrial y de Desarrollo Empresarial de Soacha, incluyendo suministro de materiales, mano de obra y servicios técnicos especializados.

A continuación, se enuncian los ítems y/o materiales entregados:

ITEM No.	7.1
NOMBRE DEL ITEM:	MOLINETE DE CONTROL DE ACCESO EN ACERO INOXIDABLE, CONTROL REMOTO, SISTEMA DE EMERGENCIA

Pruebas y verificaciones:

Prueba requerida	Descripción / Criterio técnico	Cumple (Sí/No)	Observaciones
Verificación de instalación y funcionamiento.	Pruebas funcionales: apertura, cierre, modo de emergencia. Verificación de compatibilidad con software y red. Revisión del montaje	SI	

	mecánico y pruebas de anclaje.		

Entregables:

Entregable	Requisito	Recibido (Sí/No)	Observaciones
Registro fotográfico	Antes / durante / después	SI	
Garantías	Documentación del equipo emitidos por fabricante. Garantías de fabricante.	SI	
Documentación	Manual de usuario y garantías.	SI	

Concepto de Aceptación:

X	Se recibe a satisfacción.
	Se reciben con observaciones.
	No se recibe.

Observaciones Generales:

_____
_____
_____
_____
_____

Para constancia se firma en Soacha, a los 30 días del mes de DICIEMBRE del año 2025 .

QUIEN ENTREGA:

FIRMA
Nombre: Danderley Montoya Gallego
C.C.: 16.073.065
Representa a: Consorcio AGH-C&C-SEIPRODEG Ciudad Verde
Cargo: Integrador de Sistemas
Teléfono: 315 779 4049

QUIEN RECIBE:

FIRMA
Nombre: Rodrigo Andrés Linares Bernal
C.C.:
Representa a: Interventoría
Cargo: Interventor Sistemas especiales
Teléfono: 315 284 6688

MANUALES Y GARANTÍAS

CONSORCIO
AGH-C&C-
SEIPRODEG
CIUDAD VERDE
NIT 901980651-7

DS-K3G530X
Pro Tripod Turnstile



- Motor-driven, longer service life and better traffic experience.
- Better anti-tailgating function, eliminating tailgating and accurate counting.
- Slim appearance, but also strong, showing beauty and elegance.
- Applicable to indoor and outdoor scenes, whether it is scenic spots, gyms or bus stations.
- Easy to configuration and maintenance by PC web function.

▪ Specification

System	
Motor	Brushless motor
MCBF	≥ 5 million times
Network	
Wired network	10/100 Mbps self-adaptive Ethernet
Interface	
Network interface	1
Lock control	2
Exit button	2
Alarm output	2
TAMPER	N/A
RS-485	4
RS-232	2
Wiegand	2
Fire alarm input	1
Case input	2
Hardware	
Access controller	Supplied
Supercapacitor	Supplied
Network switch	Not supplied
Capacity	
Card capacity	500,000
Event capacity	500,000
Authentication	
Card	EM card or M1 card or Desfire card (actual corresponding card type refer to product model names).
Function	
Configuration via PC Web	Support
Configuration via mobile Web	Support
Audio prompt	Support
Communication protocol	TCP/IP,ISAPI
Keypad configuration	Support
Keyfob	Support, 433 MHz/868 MHz, within 25 m
General	
Throughput	30 to 60 persons per minute The actual throughput is affected by the person passing rate and passing method.
Lane width	550 mm (21.65")
Barrier material	1.2 mm stainless pipe
Pedestal material	SUS304 stainless steel 1.5 mm,SUS304 stainless steel 1.2 mm
Power consumption	Standby: 35 W Working: 65 W Peak: 75 W
Working temperature	-20 °C to 65 °C (-4 °F to 149 °F)
Working humidity	0% to 95% (No condensing)
Protective level	IPX4

Dimensions	Without package: 1500 mm × 130 mm × 1002.5 mm (59.1" × 5.1" × 39.5") With package: 1660 mm × 510 mm × 1305 mm (65.4" × 20.1" × 51.4")
Weight	Net:52.22kg(115.13.lb);Gross:65.59kg(144.6.lb)
Approval	CE/CB/RoHS/REACH/WEEE
Power supply method	Power supply: 100 to 120 VAC~ / 200 to 240 VAC~, 50/60 Hz, 1.0-1.5A
Door open duration	5 to 60 sec
Configuration	
Lane width	550
Pedestal length	1500 mm
Module selection	YES
Pedestal width	130 mm
Wall distance	20 mm
Base	YES
Barrier material	Stainless steel pipe
Application environment	Indoor and outdoor
Authentication mode	Card,Face,QR code
Card type	EM,Desfire
Recommended width	550 mm
Base model	DS-KSM02/G530
Side pedestal	YES
Side pedestal type	Fence (130 mm)
Product type	Tripod Turnstile
Remote controller type	433Mhz,868Mhz
Movement Protrusion Width	105 mm
Door wing gap	36 mm
Door Height	Default(0.76m)
Convert Face	NO

▪ Note

The main element of the turnstile is stainless steel, which is rust less (antioxidant) and corrosion resistant (The anti-corrosion ability in the medium of acid, alkali, and salt). In order to keep the stainless steel from being oxidized or corroded, you should clean and care the turnstile surface periodically.

The instructions and tips for maintaining the turnstile are as follows:
1. Select different stainless steel types according to the variety of the environments. You can select 304 stainless steel for common circumstances and 316 stainless steel for the scenarios of seaside and chemical plants.
2. Keep the device surface clean and dry.
3. Use non-woven cloth and ethyl alcohol to clean the dirt on the device surface.
4. Use sourcing pad (do not use mesh cleaning ball) to clean the rust on the device surface by following the wire drawing on the stainless steel. And then use non-woven cloth and stainless steel cleaner to wipe the device surface.
5. Clean and maintain the device by using non-woven cloth and stainless steel cleaner periodically. It is suggested to clean the device every month in common circumstances and every week for severe environments (seaside and chemical plants for instance).


▪ Available Model

DS-K3G530X-R/MPg-Dm55

DS-K3G530X-R/EPg-Dm55


DS-K3G530X-R/M-Dm55
DS-K3G530X-R/E-Dm55
DS-K3G530X-R/M-Dm55/868
DS-K3G530X-R/Dm55/Modular
DS-K3G530X-R/Pa-Dm55/Modular
DS-K3G530X-R/DPgQ-Dm55

▪ Dimension

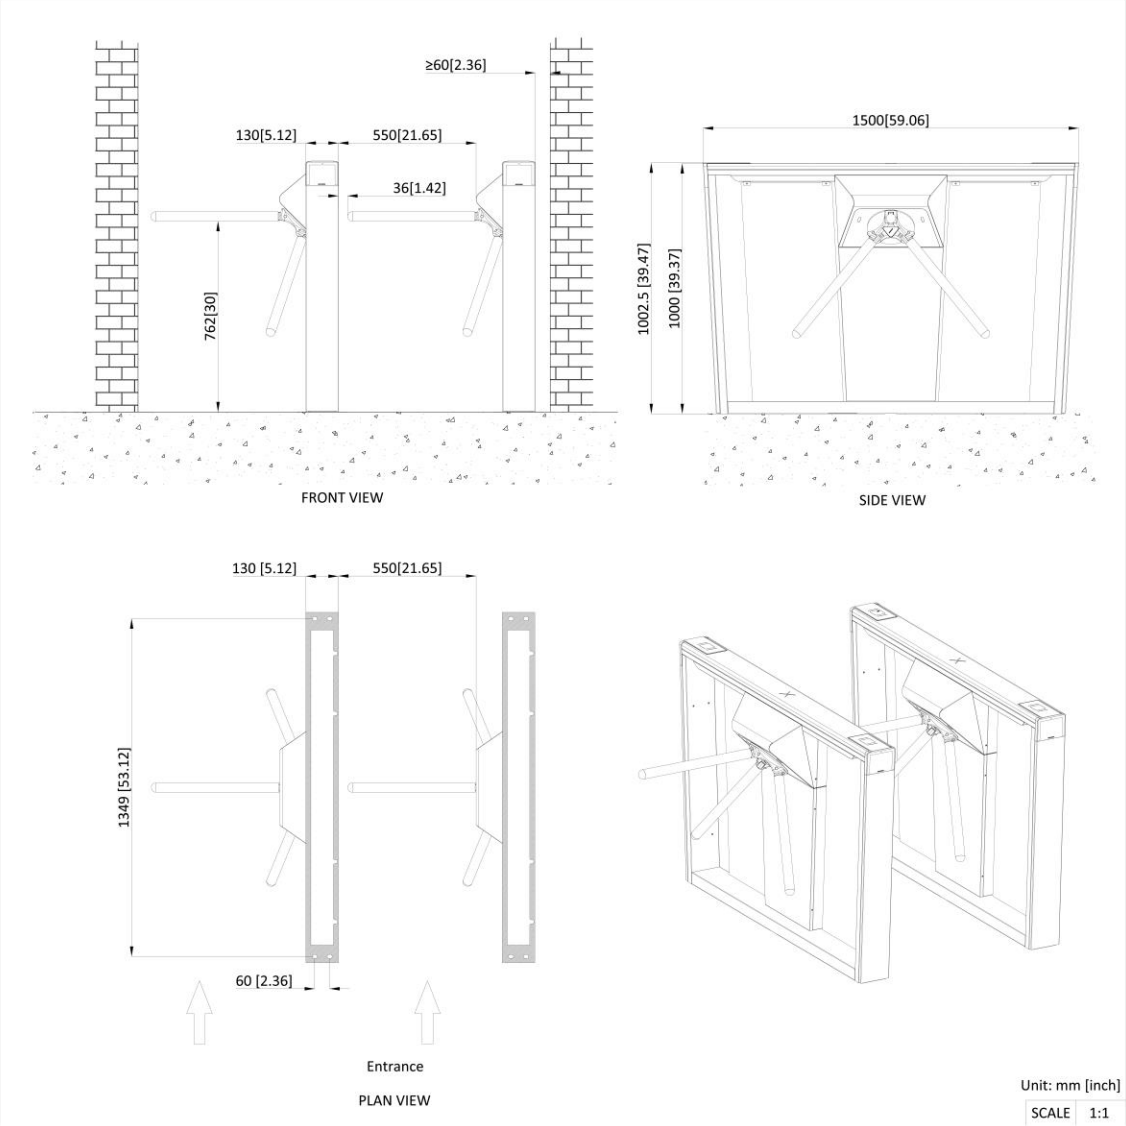

▪ Accessory

▪ Optional

DS-K7R01-868	DS-K7R01-433	DS-K7R83X	DS-KAB6-ZU3	DS-KSM02/G530
				

See Far, Go Further

www.hikvision.com
support@hikvision.com

© Hangzhou Hikvision Digital Technology Co., Ltd. Unless otherwise agreed, Hikvision makes no warranties, express or implied. We reserve the right to introduce modifications without notice.

HIKVISION®

CERTIFICADO DE GARANTIA

Fecha de emisión: 22/11/2025.
Expedida a favor de: Consorcio AGH–C&C–SEIPRODEG CIUDAD VERDE.

En referencia a los torniquetes modelo DS-K3G530X-RMPG-DM55 de HIKVISION vendidos por esta empresa de seriales:

- FN8914228
- FQ1019833
- FQ1019841

En referencia a torniquete modelo SBT2000S- SB de ZKTeco con serial:

- 300031804

CENTRO DE SOLUCIONES ELECTRONICAS SAS. Por el presente documento certificamos que los bienes entregados tienen una garantía de 100% por un periodo de UN AÑO directamente con CSE y UN AÑO adicional directamente con el fabricante HIKVISION. En torniquete maraca ZKTeco UN AÑO directamente con CSE y UN AÑO adicional directamente con el fabricante ZKTeco. No incluye manipulación por terceros ni descargas atmosféricas.

En caso de cualquier consulta o reclamo no dude en comunicarse con nosotros para hacer efectiva la garantía.

Atentamente,

Ing. Oscar Iván Guerrero Martínez
Director Técnico CSE
Móvil 316 373 7655

REGISTRO FOTOGRÁFICO

CONSORCIO
AGH-C&C-
SEIPRODEG
CIUDAD VERDE
NIT 901980651-7

7 SISTEMA CONTROL DE ACCESO (Registro Fotográfico)

7.1 MOLINETE DE CONTROL DE ACCESO EN ACERO INOXIDABLE, CONTROL REMOTO, SISTEMA DE EMERGENCIA

