
ID	Task Mode	WBS	Task Name	Duration	Start	Finish
1		1	**PROYECTO CONSEJO SUPERIOR DE LA JUDICATURA**	**205 days**	**Mon 19/01/26**	**Sat 31/10/26**
2		1.1	**INICIO**	**13,13 days**	**Mon 19/01/26**	**Wed 4/02/26**
3		1.1.1	Acta de reinicio de contrato	0,13 days	Mon 19/01/26	Mon 19/01/26
4		1.1.2	Acta aprobada	0 days	Tue 20/01/26	Tue 20/01/26
5		1.1.3	Reunion de Kick off	0,13 days	Wed 4/02/26	Thu 5/02/26
6		1.1.4	Kick off ejecutado	0 days	Thu 5/02/26	Thu 5/02/26
7		1.2	**PLANIFICACION ADMINISTRATIVA**	**2 days**	**Wed 21/01/26**	**Fri 23/01/26**
8		1.2.1	Definicion del equipo de trabajo	0,25 days	Wed 21/01/26	Thu 22/01/26
9		1.2.2	Validacion de hojas de vida	0,13 days	Thu 22/01/26	Thu 22/01/26
10		1.2.3	Envio de hojas de vida residente y electrico	0,13 days	Thu 22/01/26	Thu 22/01/26
11		1.2.4	Equipo de trabajo aprobado	0 days	Fri 23/01/26	Fri 23/01/26
12		1.3	**PLANIFICACION TECNICA**	**40,88 days**	**Mon 2/02/26**	**Mon 30/03/26**
13		1.3.1	Elaboracion de cronograma	0,25 days	Thu 5/02/26	Thu 5/02/26
14		1.3.2	Envio de fichas tecnicas	0,13 days	Mon 2/02/26	Mon 2/02/26
15		1.3.3	Reunion de verificacion de documentacion y avance	0,13 days	Wed 11/02/26	Wed 11/02/26
16		1.3.4	Programacion visitas	0,13 days	Wed 25/02/26	Wed 25/02/26
17		1.3.5	**Recorrido de levantamiento de informacion Medellin, Envigado y Rionegro**	**21 days**	**Thu 26/02/26**	**Fri 27/03/26**
18		1.3.5.1	Validacion de puntos electricos	0,38 days	Thu 26/02/26	Thu 26/02/26
19		1.3.5.2	Validacion de red de datos	0,38 days	Thu 26/02/26	Thu 26/02/26
20		1.3.5.3	Identificacion de puntos criticos de seguridad	0,38 days	Thu 26/02/26	Thu 26/02/26
21		1.3.5.4	Toma de medidas de espacio	0,38 days	Thu 26/02/26	Thu 26/02/26
22		1.3.5.5	Registro fotografico	0,38 days	Thu 26/02/26	Thu 26/02/26
23		1.3.5.6	Consolidacion de informacion tecnica	0,38 days	Thu 26/02/26	Thu 26/02/26

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress

ID	Task Mode	WBS	Task Name	Duration	Start	Finish
24		1.3.5.7	Revision de planos y puntos de instalacion	2,5 days	Mon 2/03/26	Wed 4/03/26
25		1.3.5.8	Finalizacion de visita tecnica	0 days	Fri 27/03/26	Fri 27/03/26
26		**1.3.6**	**Recorrido de levantamiento de informacion Turbo y Apartado**	**28 days**	**Thu 19/02/26**	**Mon 30/03/26**
27		1.3.6.1	Validacion de puntos electricos	0,25 days	Thu 19/02/26	Fri 20/02/26
28		1.3.6.2	Validacion de red de datos	0,25 days	Thu 19/02/26	Fri 20/02/26
29		1.3.6.3	Identificacion de puntos criticos de seguridad	0,25 days	Thu 19/02/26	Fri 20/02/26
30		1.3.6.4	Toma de medidas de espacio	0,25 days	Thu 19/02/26	Fri 20/02/26
31		1.3.6.5	Registro fotografico	0,25 days	Thu 19/02/26	Fri 20/02/26
32		1.3.6.6	Consolidacion de informacion tecnica	0,25 days	Thu 19/02/26	Fri 20/02/26
33		1.3.6.7	Revision de planos y puntos de instalacion	2,5 days	Sat 21/02/26	Thu 19/03/26
34		1.3.6.8	Definicion de rutas de canalizacion e insfraestructura	3,52 days	Thu 19/02/26	Mon 30/03/26
35		1.3.6.9	Finalizacion de visita tecnica	0 days	Fri 20/02/26	Fri 20/02/26
36		**1.4**	**INGENIERIA Y DISEÑO**	**37,88 days**	**Wed 25/03/26**	**Mon 18/05/26**
37		1.4.1	Definicion de cantidades finales	0,38 days	Wed 25/03/26	Fri 27/03/26
38		1.4.2	Ajustes de diseño (renders y planos)	1,63 days	Wed 25/03/26	Fri 10/04/26
39		1.4.3	Validacion de site survey	0,25 days	Tue 7/04/26	Wed 8/04/26
40		1.4.4	Correccion y ajustes de site survey	4,27 days	Tue 31/03/26	Fri 15/05/26
41		1.4.5	Aprobacion de diseños e informe de site survey	0 days	Mon 18/05/26	Mon 18/05/26
42		1.4.6	Aprobacion de cronograma	0 days	Mon 18/05/26	Mon 18/05/26
43		**1.5**	**ADQUISICION Y LOGISTICA**	**102 days**	**Mon 30/03/26**	**Tue 18/08/26**
44		**1.5.1**	**Gestion de compras Internacionales**	**102 days**	**Mon 30/03/26**	**Tue 18/08/26**
45		1.5.1.1	Orden de compra e Importacion	90,13 days	Mon 30/03/26	Fri 31/07/26
46		1.5.1.2	Nacionalizacion	10 days	Mon 3/08/26	Fri 14/08/26

Project: Cronograma estimado_
Date: Fri 10/07/26



ID	Task Mode	WBS	Task Name	Duration	Start	Finish
47		1.5.1.3	Recepcion e inspeccion de equipos	3 days	Fri 14/08/26	Tue 18/08/26
48		1.5.1.4	Entrega de equipos sedes	0 days	Tue 18/08/26	Tue 18/08/26
49		**1.5.2**	**Gestion de compras nacionales**	**85 days**	**Mon 30/03/26**	**Fri 24/07/26**
50	✓	1.5.2.1	Orden de compra	80 days	Mon 30/03/26	Fri 17/07/26
51		1.5.2.2	Recepcion e inspeccion de equipos	5 days	Mon 20/07/26	Fri 24/07/26
52		1.5.2.3	Entrega de equipos en sede	0 days	Fri 24/07/26	Fri 24/07/26
53		**1.6**	**IMPLEMENTACION JOSE FELIX RESTREPO - MEDELLIN**	**104 days**	**Mon 4/05/26**	**Thu 24/09/26**
54	✓	1.6.1	Alistamiento de infraestructura	5 days	Mon 18/05/26	Fri 22/05/26
55	✓	1.6.2	Canalizaciones, nucleos aprobados por la supervision	0 days	Mon 18/05/26	Mon 18/05/26
56	✓	**1.6.3**	**Perforaciones cuartos tecnicos**	**27 days**	**Mon 4/05/26**	**Tue 9/06/26**
57	✓	1.6.3.1	Piso 1, 4, 9, 12	5 days	Mon 4/05/26	Fri 15/05/26
58	✓	1.6.3.2	Piso 14, 16, 18, 21	8 days	Fri 15/05/26	Tue 26/05/26
59	✓	1.6.3.3	Piso 23, 25, 27	6 days	Wed 27/05/26	Wed 3/06/26
60	✓	1.6.3.4	Piso 3	5 days	Wed 3/06/26	Tue 9/06/26
61		**1.6.4**	**Perforacion pasos hacia canastilla**	**16 days**	**Mon 29/06/26**	**Mon 20/07/26**
62	✓	1.6.4.1	Piso 25, 27	2 days	Mon 29/06/26	Tue 30/06/26
63		1.6.4.2	Piso 18, 21, 23	8 days	Wed 1/07/26	Fri 10/07/26
64		1.6.4.3	Piso 12, 14, 16	3 days	Mon 13/07/26	Wed 15/07/26
65		1.6.4.4	Piso 1, 4, 9	3 days	Thu 16/07/26	Mon 20/07/26
66		**1.6.5**	**Instalacion de infraestructura y cableado CCTV**	**34 days**	**Thu 11/06/26**	**Tue 28/07/26**
67	✓	1.6.5.1	Piso 27 y 28	4 days	Thu 11/06/26	Tue 16/06/26
68	✓	1.6.5.2	Piso 25 y 26	2 days	Mon 15/06/26	Tue 16/06/26
69	✓	1.6.5.3	Piso 23 y 24	2 days	Tue 16/06/26	Wed 17/06/26

Project: Cronograma estimado_
Date: Fri 10/07/26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Critical	
Project Summary		Manual Summary		Critical Split	
Inactive Task		Start-only		Progress	
Inactive Milestone		Finish-only		Manual Progress	


ID	Task Mode	WBS	Task Name	Duration	Start	Finish
70		1.6.5.4	Piso 21 y 22	2 days	Thu 18/06/26	Fri 19/06/26
71		1.6.5.5	Piso 19 y 20	2 days	Mon 22/06/26	Tue 23/06/26
72		1.6.5.6	Piso 17 y 18	2 days	Tue 23/06/26	Wed 24/06/26
73		1.6.5.7	Piso 15 y 16	2 days	Wed 24/06/26	Thu 25/06/26
74		1.6.5.8	Piso 13 y 14	2 days	Thu 25/06/26	Fri 26/06/26
75		1.6.5.9	Piso 11 y 12	2 days	Fri 26/06/26	Mon 29/06/26
76		1.6.5.10	Piso 9 y 10	2 days	Mon 29/06/26	Tue 30/06/26
77		1.6.5.11	Piso 7 y 8	2 days	Mon 13/07/26	Tue 14/07/26
78		1.6.5.12	Piso 5 y 6	2 days	Wed 15/07/26	Thu 16/07/26
79		1.6.5.13	Piso 3 y 4	2 days	Fri 17/07/26	Mon 20/07/26
80		1.6.5.14	Piso 1 y 2	2 days	Tue 21/07/26	Wed 22/07/26
81		1.6.5.15	Sotano	4 days	Thu 23/07/26	Tue 28/07/26
82		1.6.5.16	Cierre de Instalacion de infraestructura pisos	0 days	Tue 28/07/26	Tue 28/07/26
83		**1.6.6**	**Instalacion de backbone de fibra**	**6 days**	**Mon 6/07/26**	**Mon 13/07/26**
84		1.6.6.1	Piso 1, 4, 9, 12	1 day	Mon 6/07/26	Mon 6/07/26
85		1.6.6.2	Piso 14, 16, 18, 21	1 day	Tue 7/07/26	Tue 7/07/26
86		1.6.6.3	Piso 23, 25, 27	1 day	Wed 8/07/26	Wed 8/07/26
87		1.6.6.4	Piso 3	3 days	Thu 9/07/26	Mon 13/07/26
88		1.6.6.5	Certificacion tecnica de enlaces de fibra	0 days	Mon 13/07/26	Mon 13/07/26
89		**1.6.7**	**Instalacion de switches**	**5 days**	**Mon 24/08/26**	**Fri 28/08/26**
90		1.6.7.1	Piso 1, 4, 9	1 day	Mon 24/08/26	Mon 24/08/26
91		1.6.7.2	Piso 12, 14, 16	1 day	Tue 25/08/26	Tue 25/08/26
92		1.6.7.3	Piso 18, 21, 23	1 day	Wed 26/08/26	Wed 26/08/26

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress


ID	Task Mode	WBS	Task Name	Duration	Start	Finish
93		1.6.7.4	Piso 25, 27	1 day	Thu 27/08/26	Thu 27/08/26
94		1.6.7.5	Piso 3 - Sala de monitoreo	1 day	Fri 28/08/26	Fri 28/08/26
95		1.6.7.6	Certificacion de puntos de datos camaras	5 days	Mon 24/08/26	Fri 28/08/26
96		**1.6.8**	**Instalacion de camaras CCTV**	**11 days**	**Mon 17/08/26**	**Mon 31/08/26**
97		1.6.8.1	Piso 1, 2, 3	1 day	Mon 17/08/26	Mon 17/08/26
98		1.6.8.2	Piso 4, 5, 6	1 day	Tue 18/08/26	Tue 18/08/26
99		1.6.8.3	Piso 7, 8, 9	1 day	Wed 19/08/26	Wed 19/08/26
100		1.6.8.4	Piso 10, 11, 12	1 day	Thu 20/08/26	Thu 20/08/26
101		1.6.8.5	Piso 13, 14, 15	1 day	Fri 21/08/26	Fri 21/08/26
102		1.6.8.6	Piso 16, 17, 18	1 day	Sat 22/08/26	Sat 22/08/26
103		1.6.8.7	Piso 19, 20, 21	1 day	Mon 24/08/26	Mon 24/08/26
104		1.6.8.8	Piso 22, 23, 24	1 day	Tue 25/08/26	Tue 25/08/26
105		1.6.8.9	Piso 25, 26, 27, 28	1 day	Wed 26/08/26	Wed 26/08/26
106		1.6.8.10	Sotano	3 days	Thu 27/08/26	Mon 31/08/26
107		1.6.9	Instalacion NVR/VMS y estaciones de trabajo	5 days	Fri 28/08/26	Thu 3/09/26
108		1.6.10	Equipos activos y energizados	0 days	Thu 3/09/26	Thu 3/09/26
109		**1.6.11**	**Instalacion de infraestructura y cableado control de acceso**	**16 days**	**Mon 24/08/26**	**Mon 14/09/26**
110		1.6.11.1	Ingreso visitantes	5 days	Mon 24/08/26	Fri 28/08/26
111		1.6.11.2	Ingreso funcionarios	5 days	Mon 31/08/26	Fri 4/09/26
112		1.6.11.3	Ingreso movilidad reducida	4 days	Mon 7/09/26	Thu 10/09/26
113		1.6.11.4	Salida	3 days	Thu 10/09/26	Mon 14/09/26
114		**1.6.12**	**Instalacion control de acceso**	**10 days**	**Tue 1/09/26**	**Mon 14/09/26**
115		1.6.12.1	Pasillos motorizados	8 days	Tue 1/09/26	Thu 10/09/26

Project: Cronograma estimado_
Date: Fri 10/07/26




ID	Task Mode	WBS	Task Name	Duration	Start	Finish
116		1.6.12.2	Maquina de rayos x	2 days	Thu 10/09/26	Fri 11/09/26
117		1.6.12.3	Arcos de deteccion	1 day	Mon 14/09/26	Mon 14/09/26
118		1.6.13	Integracion de sistema	3 days	Tue 15/09/26	Thu 17/09/26
119		1.6.14	Pruebas tecnicas y capacitacion	5 days	Fri 18/09/26	Thu 24/09/26
120		1.6.15	Puesta en operacion Medellin (ATP)	0 days	Fri 18/09/26	Fri 18/09/26
121		**1.7**	**IMPLEMENTACION ENVIGADO**	**19 days**	**Sat 19/09/26**	**Fri 16/10/26**
122		1.7.1	Alistamiento de infraestructura	5 days	Sat 19/09/26	Thu 24/09/26
123		1.7.2	Instalacion de infraestructura y cableado control de acceso	15 days	Sat 19/09/26	Thu 8/10/26
124		1.7.3	Instalacion VMS	3 days	Mon 21/09/26	Wed 23/09/26
125		1.7.4	Instalacion control de acceso	5 days	Mon 21/09/26	Fri 25/09/26
126		1.7.5	Integracion de sistema	2 days	Thu 8/10/26	Fri 9/10/26
127		1.7.6	Pruebas tecnicas y capacitacion	2 days	Sat 10/10/26	Mon 12/10/26
128		1.7.7	Puesta en operacion Envigado	0 days	Fri 16/10/26	Fri 16/10/26
129		**1.8**	**IMPLEMENTACION RIONEGRO**	**0 days**	**Fri 16/10/26**	**Fri 16/10/26**
130		1.8.1	Alistamiento de infraestructura			
131		1.8.2	Instalacion de cableado			
132		1.8.3	Instalacion de camaras CCTV			
133		1.8.4	Instalacion NVR/VMS			
134		1.8.5	Instalacion control de acceso			
135		1.8.6	Integracion de sistema			
136		1.8.7	Pruebas tecnicas			
137		1.8.8	Puesta en operacion Envigado			
138		**1.9**	**IMPLEMENTACION TURBO**	**19 days**	**Mon 21/09/26**	**Fri 16/10/26**

Project: Cronograma estimado_
Date: Fri 10/07/26




ID	Task Mode	WBS	Task Name	Duration	Start	Finish
139		1.9.1	Alistamiento de infraestructura	6 days	Mon 21/09/26	Mon 28/09/26
140		1.9.2	Instalacion de infraestructura y cableado CCTV	10 days	Mon 21/09/26	Fri 2/10/26
141		1.9.3	Instalacion de camaras CCTV	8 days	Mon 28/09/26	Wed 7/10/26
142		1.9.4	Instalacion NVR/VMS	1 day	Wed 7/10/26	Wed 7/10/26
143		1.9.5	Instalacion de infraestructura y cableado control de acceso	5 days	Thu 1/10/26	Wed 7/10/26
144		1.9.6	Instalacion control de acceso	4 days	Wed 7/10/26	Mon 12/10/26
145		1.9.7	Integracion de sistema	1 day	Mon 12/10/26	Mon 12/10/26
146		1.9.8	Pruebas tecnicas y capcitacion	1 day	Tue 13/10/26	Tue 13/10/26
147		1.9.9	Puesta en operacion Turbo	0 days	Fri 16/10/26	Fri 16/10/26
148		**1.10**	**IMPLEMENTACION APARTADO**	**21 days**	**Mon 28/09/26**	**Mon 26/10/26**
149		1.10.1	Alistamiento de infraestructura	5 days	Mon 28/09/26	Fri 2/10/26
150		1.10.2	Instalacion de cableado	10 days	Mon 5/10/26	Fri 16/10/26
151		1.10.3	Instalacion VMS	3 days	Fri 16/10/26	Tue 20/10/26
152		1.10.4	Instalacion control de acceso	5 days	Wed 14/10/26	Tue 20/10/26
153		1.10.5	Integracion de sistema	2 days	Wed 21/10/26	Thu 22/10/26
154		1.10.6	Pruebas tecnicas y capacitacion	2 days	Fri 23/10/26	Mon 26/10/26
155		1.10.7	Puesta en operacion Apartado	0 days	Mon 26/10/26	Mon 26/10/26
156		**1.11**	**CIERRE**	**22 days**	**Thu 1/10/26**	**Sat 31/10/26**
157		1.11.1	Aprobacion final del sistema	18 days	Thu 1/10/26	Mon 26/10/26
158		1.11.2	Entrega de documentacion (informe, manuales etc)	9 days	Wed 14/10/26	Mon 26/10/26
159		1.11.3	Ajuste de correccion de documentacion	8 days	Wed 21/10/26	Fri 30/10/26
160		1.11.4	Acta de cierre del proyecto	0 days	Sat 31/10/26	Sat 31/10/26

Project: Cronograma estimado_
Date: Fri 10/07/26




Predecess	% Complete
	48%
	100%
	100%
3	100%
4	100%
5	100%
	100%
	100%
8	100%
9	100%
10	100%
	100%
	100%
	100%
14	100%
	100%
	100%
15	100%
18	100%
19	100%
20	100%
21	100%
22	100%

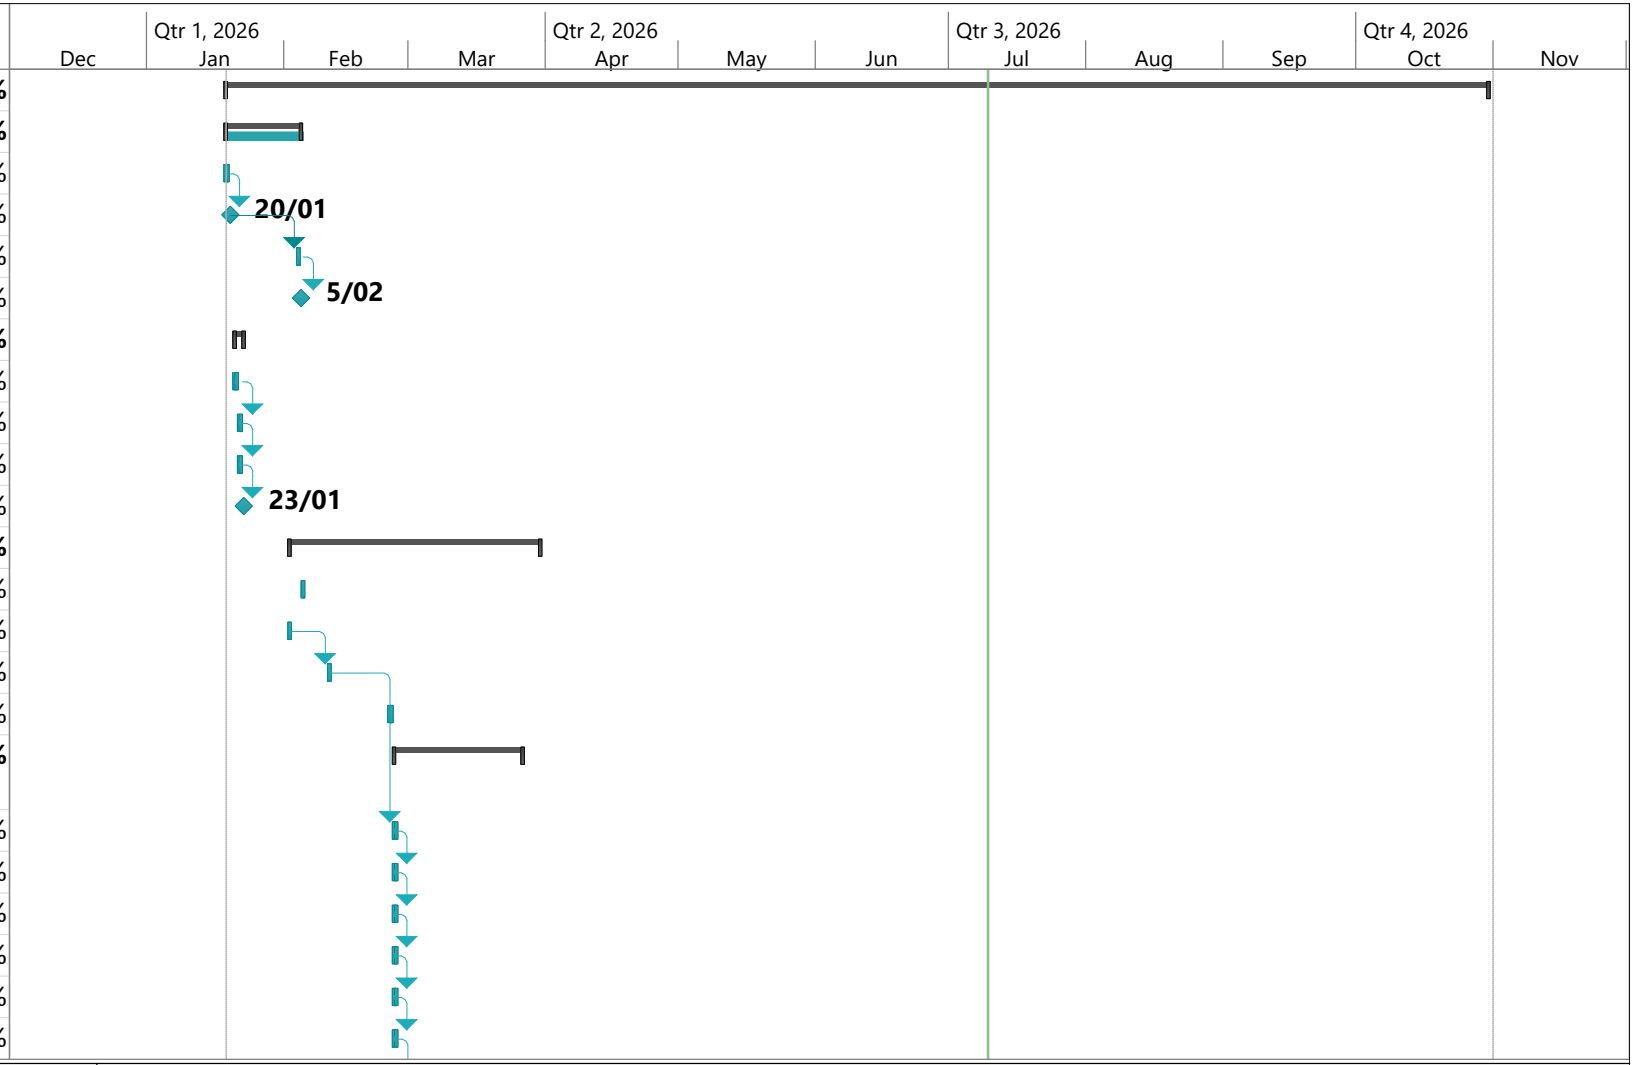

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress


Predecess	% Complete
23	100%
	100%
	100%
25	100%
27	100%
28	100%
29	100%
30	100%
31	100%
	100%
	100%
	100%
	100%
	100%
	100%
37	100%
	100%
40	100%
41	100%
	85%
37	**78%**
37	89%
45	0%

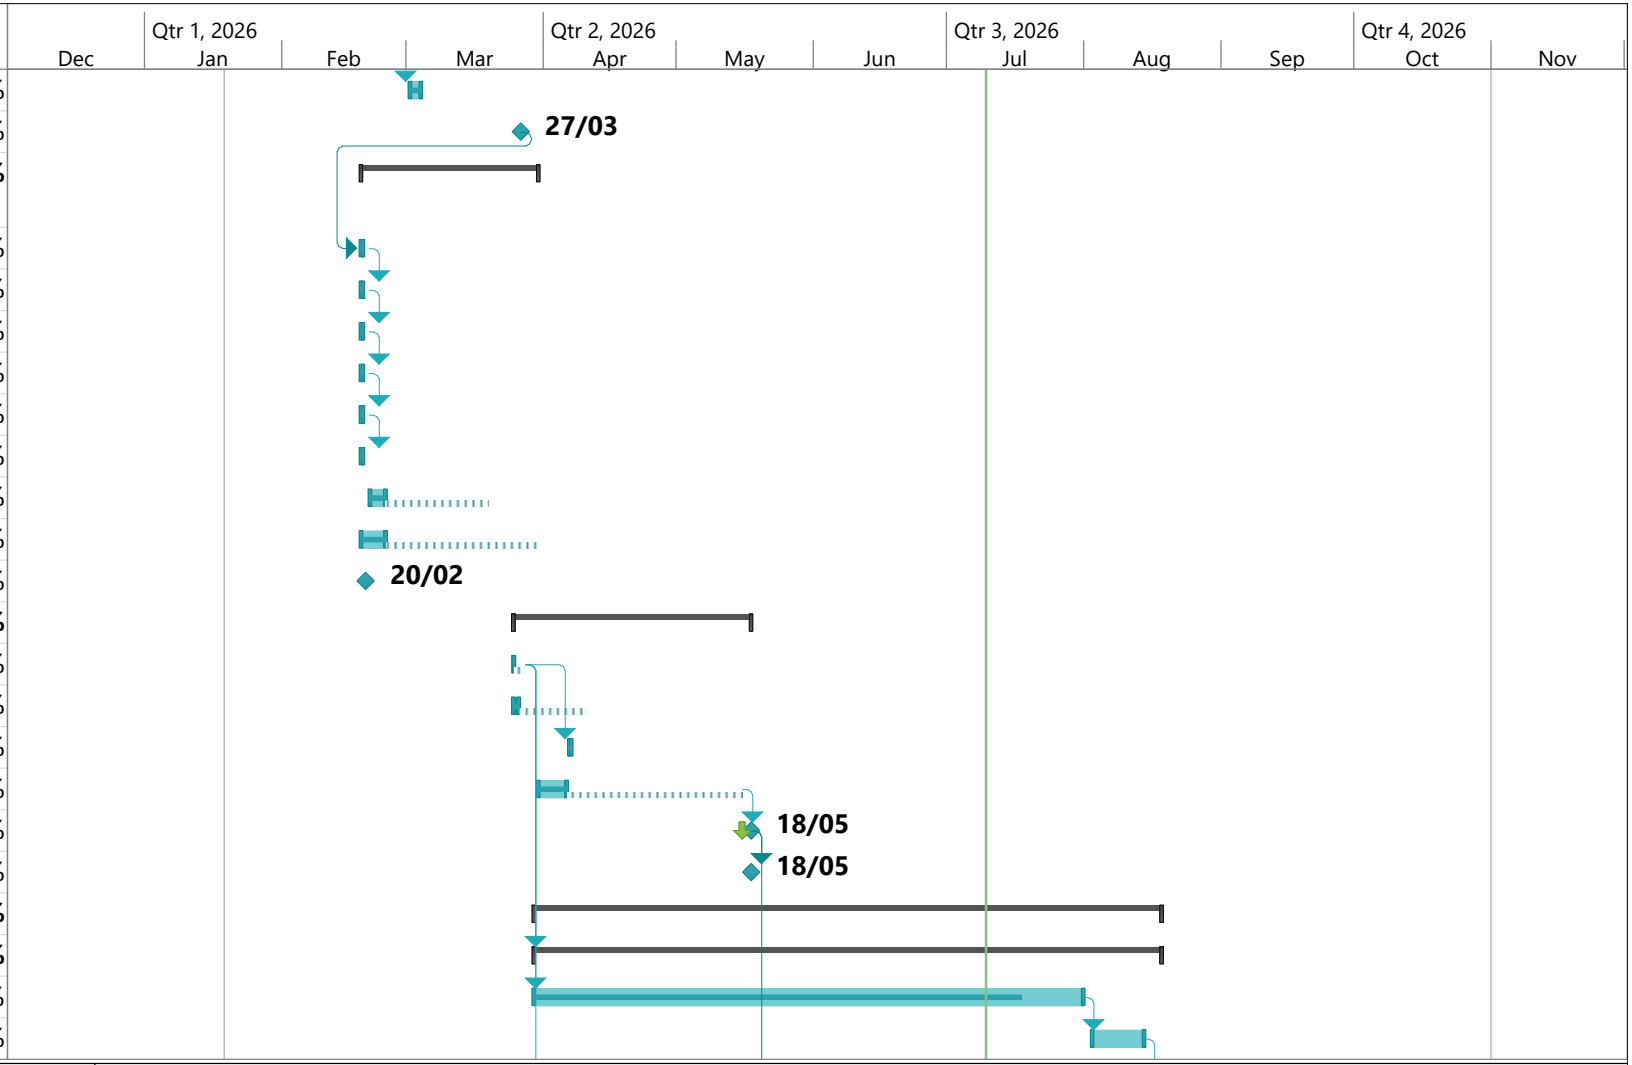

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress


Predecess	% Complete
46	0%
47	0%
	94%
37	100%
	0%
51	0%
	36%
41	100%
54	100%
55	**100%**
55	100%
57	100%
58	100%
59	100%
	17%
	100%
62	9%
63	0%
64	0%
56	**65%**
60	100%
67	100%
68	100%

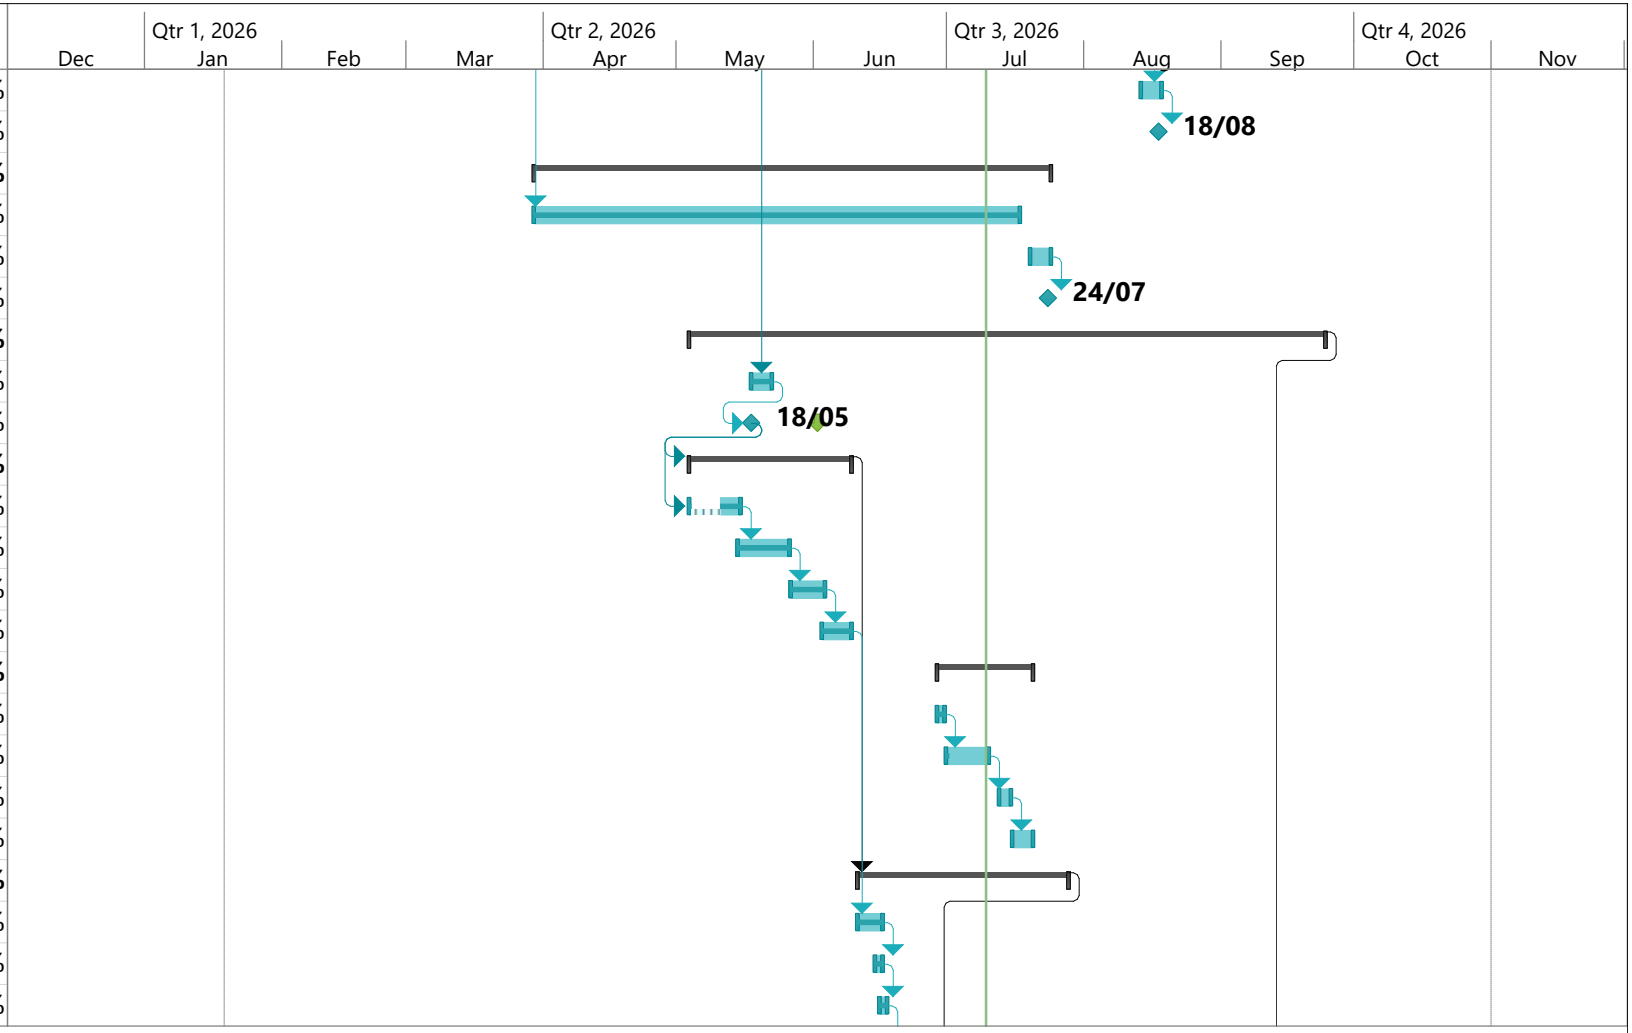

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress


Predecess	% Complete
69	100%
70	100%
71	100%
72	100%
73	100%
74	100%
75	100%
76	0%
77	0%
78	0%
79	0%
80	0%
81	0%
66	**0%**
76	0%
84	0%
85	0%
86	0%
87	0%
83	**0%**
88	0%
90	0%
91	0%

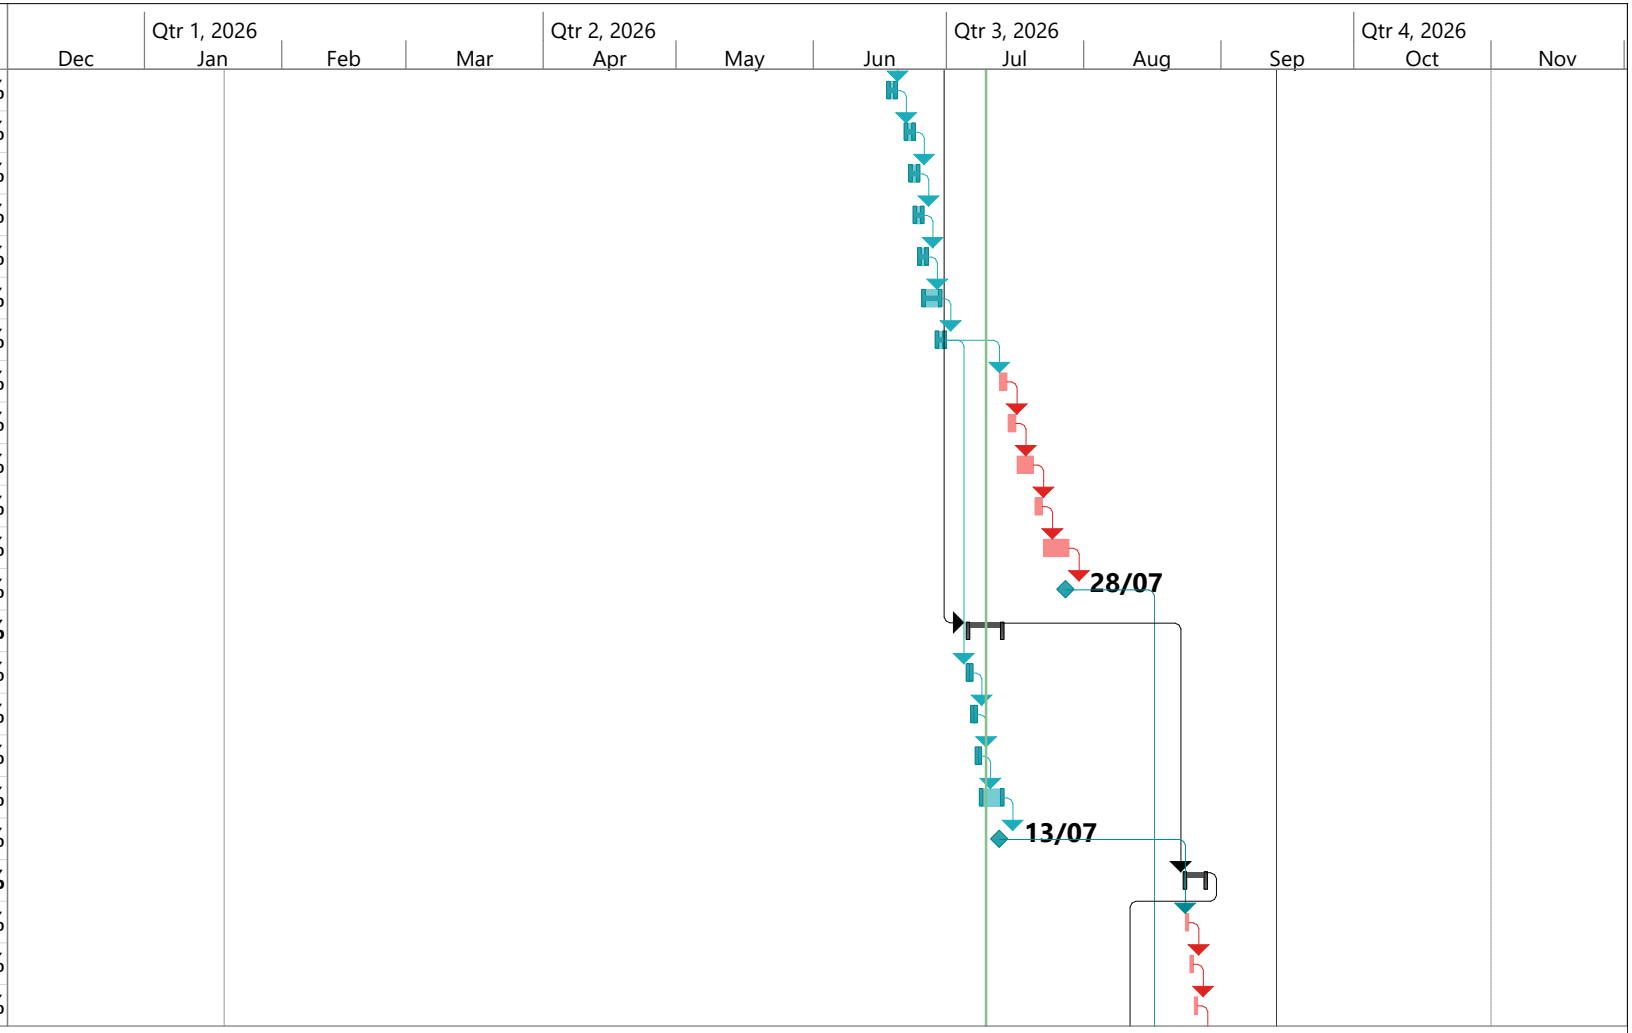

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress


Predecess	% Complete
92	0%
93	0%
	0%
89	**0%**
82	0%
97	0%
98	0%
99	0%
100	0%
101	0%
102	0%
103	0%
104	0%
105	0%
96	0%
107	0%
108	**0%**
	0%
110	0%
111	0%
112	0%
109	**0%**
110	0%

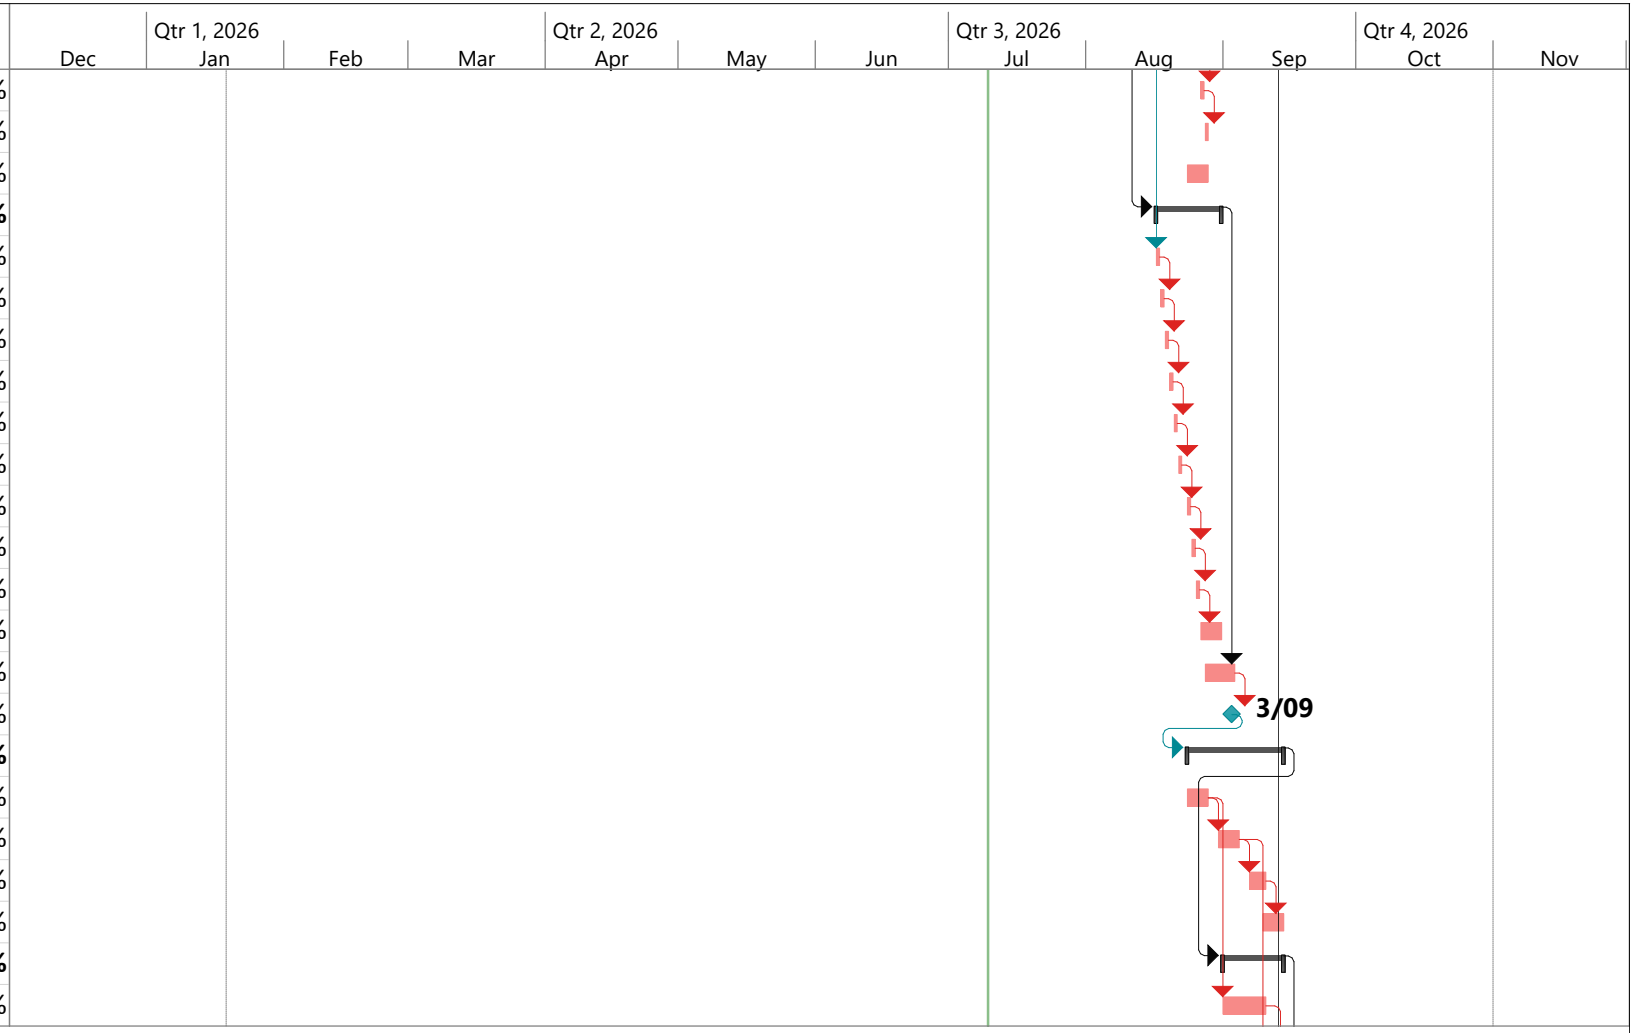

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress

Predecess	% Complete
111	0%
115	0%
114	0%
118	0%
119	0%
53	**0%**
	0%
122	0%
123	0%
124	0%
125	0%
126	0%
127	0%
121	**0%**
	0%
	0%
	0%
	0%
	0%
	0%
	0%
	0%
129	**0%**

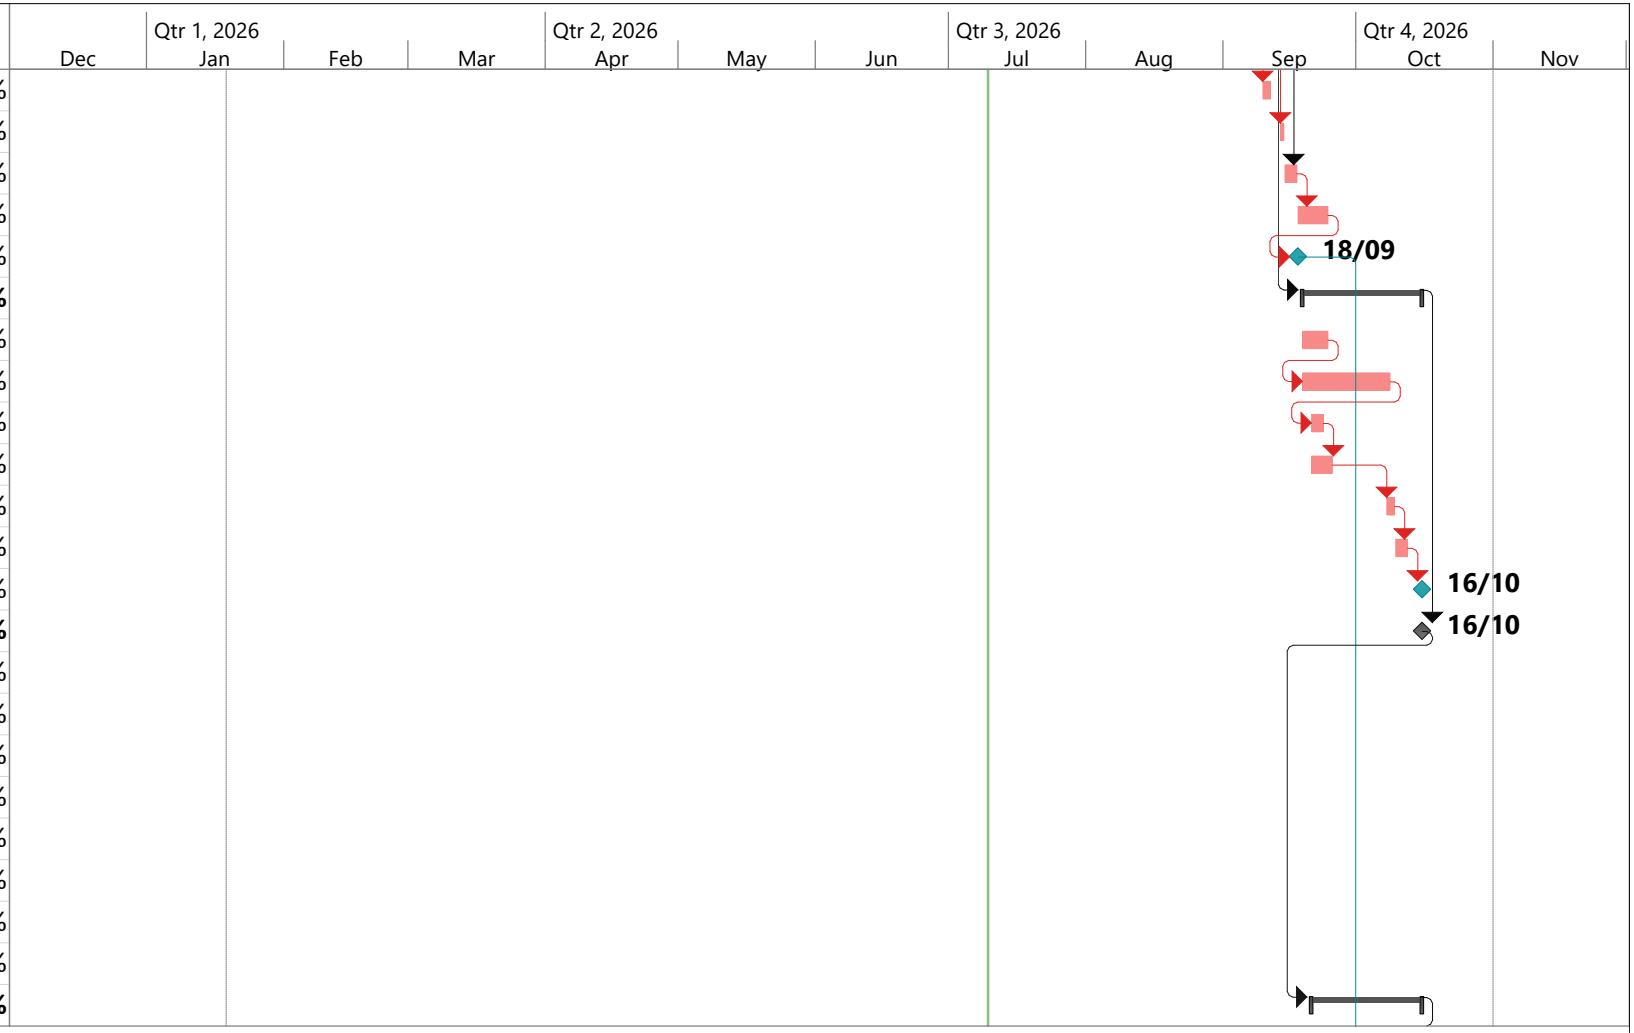

Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress

Predecess	% Complete
	0%
139	0%
140	0%
141	0%
142	0%
143	0%
144	0%
145	0%
146	0%
138	**0%**
	0%
149	0%
150	0%
151	0%
152	0%
153	0%
154	0%
148	**0%**
120	0%
157	0%
158	0%
159	0%



Project: Cronograma estimado_
Date: Fri 10/07/26

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Critical
Project Summary	Manual Summary	Critical Split
Inactive Task	Start-only	Progress
Inactive Milestone	Finish-only	Manual Progress
